




# CORE.NV Project

May Status Report

June 10, 2025





# Agenda



- Production Operations
- Executive Summary
- Risks Heat Map and Risks Register
- Project Deliverable Summary
- 90-Day Look Ahead
- Accomplishments
- Questions?





# Production Operations



- Annual close activities in flight
- Monthly steady state (SLA) meetings
- Manual Disbursement transaction work
- [REDACTED]
- Weekly calls with SCO, Treasury and Finance continue
- Budget Status Report stable and in use





**State of Nevada - Advantage Cloud Scorecard**  
**Contract Year: October 2024 - September 2025**

[illegible]

SLA Client Credits															
CGI Client Credits Issued				N/A	N/A	N/A	N/A								

<b>KEY to CHART</b>
<b>Met or Exceeded Expected SLA</b>
<b>Below Minimum Service Level</b>

NOTES



# Executive Summary

CORE.NV			
Status Date	6/10/2025	Reporting Period	5/1/2025 – 5/31/2025
Overall Status		Scope and Risk categories associated with go-live are being mitigated.	
Schedule		On track, currently executing mock conversion #2. NeoGov project kickoff.	
Resources		CGI additional resources are tasked, continue to add to LSS team.	
Scope		Pending decision on NDOT go live date.	
Risks		The teams continue to monitor and mitigate multiple high-priority risks.	
Issues		Monitoring Advantage 2 stability.	
Budget		No change to planned budget.	



Green = On schedule



Yellow = Delayed




Red = Significant blockers



# Risks Heat Map

Project Risks are Logged and Maintained in Jira. Heat Map metrics are as of 6/2/2025.

## Metrics and Heat Map

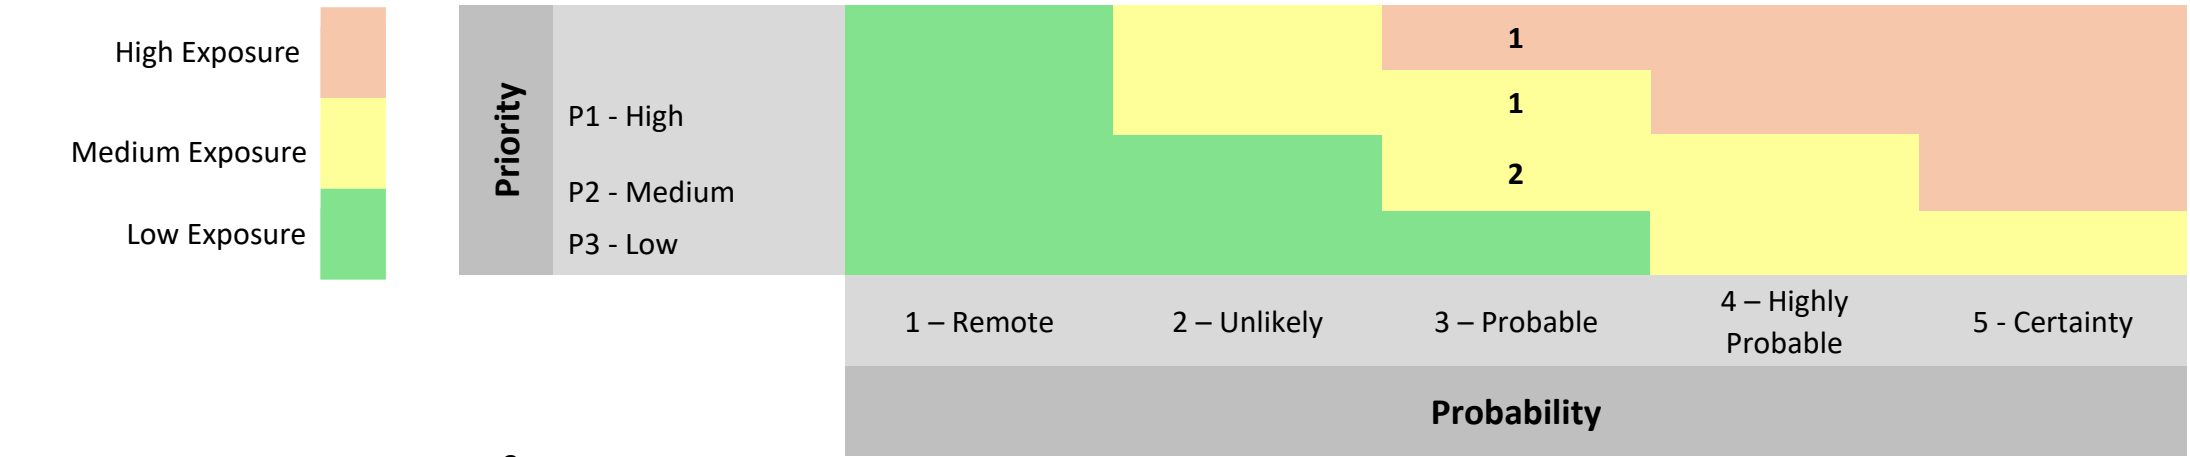

In Review Candidates: 9

Open Risks: 4

Closed Risks since last session: 1





# Risks Register

Project Risks are logged and maintained in Jira. Table was pulled 6/2/2025.

Risk #	Description	Status	Response Status	Priority	Probability	Severity
[REDACTED]	[REDACTED]	[REDACTED] [REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]
[REDACTED]	[REDACTED]	[REDACTED] [REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]
[REDACTED]	[REDACTED]	[REDACTED] [REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]
[REDACTED]	[REDACTED] [REDACTED] [REDACTED]	[REDACTED] [REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]





# May Project Deliverable Status

Statuses as of 6/2/2025.

Deliverable / Work Product	Status	Percent Complete	Invoice Period	Current Status
P1B Readiness Assessment Checklist	Delivered	100%	5/2025	✓ Approved
EUT Monthly Progress Report April	Delivered	100%	5/2025	✓ Approved
P1B Performance Test Execution Month 1	Delivered	100%	5/2025	✓ Approved
P1B Performance Test Execution Month 2	Delivered	100%	5/2025	✓ Approved
Monthly Status Report #19	Delivered	100%	5/2025	✓ Approved
P1B Performance Test Results	Delivered	100%	5/2025	✓ In review
P1B UAT Support Month 4 (Parallel Payroll)	Delivered	100%	5/2025	✓ In review







# 90-Day Look Ahead\*

Deliverables/Work Products/Milestones



## June 2025

- Monthly Status Report #20 – Submission 6/3/2025
- P1B UAT Support Month 3 – 6/6/2025
- P1B Performance Test Execution Month 3 (Results) – 6/11/2025
- EUT Monthly Progress Report May – Submission 6/12/2025
- P1B Build Stage Complete – 6/20/2025
- Readiness Assessment – Complete 6/23/2025
- P1B Cutover Plan and Checklist – Submission 6/24/2025

## July 2025

- Monthly Status Report #21 – Submission 7/2/2025
- EUT Monthly Progress Report June – Submission 7/10/2025

## August 2025

- Monthly Status Report #22 – Submission 8/4/2025
- EUT Monthly Progress Report July – Submission 8/14/2025

\* Dates are subject to P1B schedule updates, which are in progress.





## Financial (FIN) Advantage 4 Accomplishments



- The focus for the Financial team was on a successful PI8 Planning event and UAT support for NDOT.
  - Provided training to SCO/STO on how to add new bank accounts
  - NDOT UAT round 2
  - Completed 3 NDOT recap series
  - Supporting annual close activities in flight





# Human Resource Management (HRM) Advantage 4 Accomplishments



- The focus for the HRM team was on a successful PI8 Planning event and Parallel Payroll execution.
  - Parallel Payroll #3 near completion
  - EUAT for Department Security and Workflow testing
    - Personnel Management testing successful
  - MICR changes completed, await subsequent validation with [REDACTED]
  - Mock Conversion #2
  - Completed three (3) Readiness Assessments for the Oct go live





# Questions?

